



Rocky Mountain Balance Co.

Test and Balance Services
NEBB Certified

13464 Virgo Ct.
Littleton, CO. 80124
Phone: (303) 623-7648
Fax. (303) 662-8477

Test and Balance Report

*J.P. Morgan
Chase Bank*

CO Springs, Colorado

**CERTIFICATION**PROJECT J.P. Morgan Chase BankADDRESS 1st Floor - Retail Bank T.I.
28 East Boulder Street, Suite 100
Colorado Springs, CO 80909

THE DATA PRESENTED IN THIS REPORT IS AN EXACT RECORD OF SYSTEM PERFORMANCE AND WAS OBTAINED IN ACCORDANCE WITH NEBB STANDARD PROCEDURES. ANY VARIANCES FROM DESIGN QUANTITIES WHICH EXCEED NEBB TOLERANCES ARE NOTED THROUGHOUT THIS REPORT.

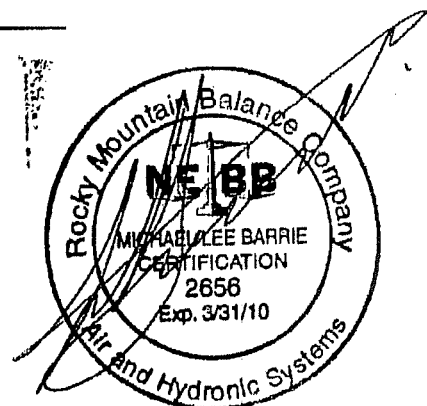
THE AIR DISTRIBUTION SYSTEMS HAVE BEEN TESTED & BALANCED AND FINAL ADJUSTMENTS HAVE BEEN MADE IN ACCORDANCE WITH NEBB "PROCEDURAL STANDARDS FOR TESTING--ADJUSTING--BALANCING OF ENVIRONMENTAL SYSTEMS" AND THE PROJECT SPECIFICATIONS.

NEBB CONTRACTOR Rocky Mountain Balance Co.REG. NO. 2656 CERTIFIED BY Michael L. Barrie DATE Feb. 23, 2010

THE HYDRONIC DISTRIBUTION SYSTEMS HAVE BEEN TESTED & BALANCED AND FINAL ADJUSTMENTS HAVE BEEN MADE IN ACCORDANCE WITH NEBB "PROCEDURAL STANDARDS FOR TESTING--ADJUSTING--BALANCING OF ENVIRONMENTAL SYSTEMS" AND THE PROJECT SPECIFICATIONS.

NEBB CONTRACTOR Rocky Mountain Balance Co.REG. NO. 2656 CERTIFIED BY Michael L. Barrie DATE Feb. 23, 2010

SUBMITTED & CERTIFIED BY:

NEBB CONTRACTOR Rocky Mountain Balance Co.TAB SUPERVISOR Michael L. BarrieREG. NO. 2656DATE Feb. 23, 2010



AIR OUTLET TEST REPORT

PROJECT J.P. Morgan Chase BankSYSTEM ExistingTEST APPARATUS Shortridge Multimeter

AREA SERVED	OUTLET				DESIGN		PRELIMINARY		MIN		FINAL		REMARKS
	NO.	TYPE	SIZE	AK	CFM	VEL	VEL	CFM	DES	ACT	VEL	CFM	
VAV-101													
	1	Slot	4'	1.0	125			167				130	
	2	Slot	4'	1.0	125			136				125	
	3	Slot	4'	1.0	125			119				122	
	4	Slot	4'	1.0	125			108				126	
	5	Slot	4'	1.0	125			185				128	
	6	CD	24x24	1.0	450			330				427	
	7	CD	24x24	1.0	200			300				193	
												1251	
VAV-102													
	1	Slot	4'	1.0	125			112				118	
	2	Slot	4'	1.0	125			96				117	
	3	Slot	4'	1.0	125			116				123	
	4	Slot	4'	1.0	125			87				134	
	5	Slot	4'	1.0	125			75				122	
	6	Slot	4'	1.0	125			79				118	
	7	CD	24x24	1.0	200			250				203	
	8	CD	24x24	1.0	200			249				191	
	9	CD	24x24	1.0	200			269				195	
	10	CD	24x24	1.0	200			211				192	
Total					1550							1513	

REMARKS:

TEST DATE: 2/23/10

READINGS BY

LB

Rocky Mountain Balance Co.



AIR OUTLET TEST REPORT

PROJECT J.P. Morgan Chase BankSYSTEM ExistingTEST APPARATUS Shortridge Multimeter

AREA SERVED	OUTLET				DESIGN		PRELIMINARY		MIN		FINAL		REMARKS
	NO.	TYPE	SIZE	AK	CFM	VEL	VEL	CFM	DES	ACT	VEL	CFM	
VAV-103													
	1	CD	24x24	1.0	250			282				266	
	2	CD	24x24	1.0	250			276				260	
	3	CD	24x24	1.0	250			243				259	
	4	CD	24x24	1.0	250			240				265	
Total					1000							1050	
VAV-104													
	1	CD	24x24	1.0	200			227				207	
	2	CD	24x24	1.0	200			249				206	
	3	CD	24x24	1.0	200			183				189	
	4	CD	24x24	1.0	200			210				206	
	5	CD	24x24	1.0	200			192				199	
Total					1000							1007	
VAV-105													
	1	CD	24x24	1.0	200			78				198	
	2	CD	24x24	1.0	100			214				109	
Total					300							307	

REMARKS:

TEST DATE: 2/18/10

READINGS BY

LB

Rocky Mountain Balance Co.



LOCATION Varies

[illegible]

READINGS BY: LB
Rocky Mountain Balance Co.
